


# RFQ Testing Timeline

C.Y. Tan  
13 Apr 2011

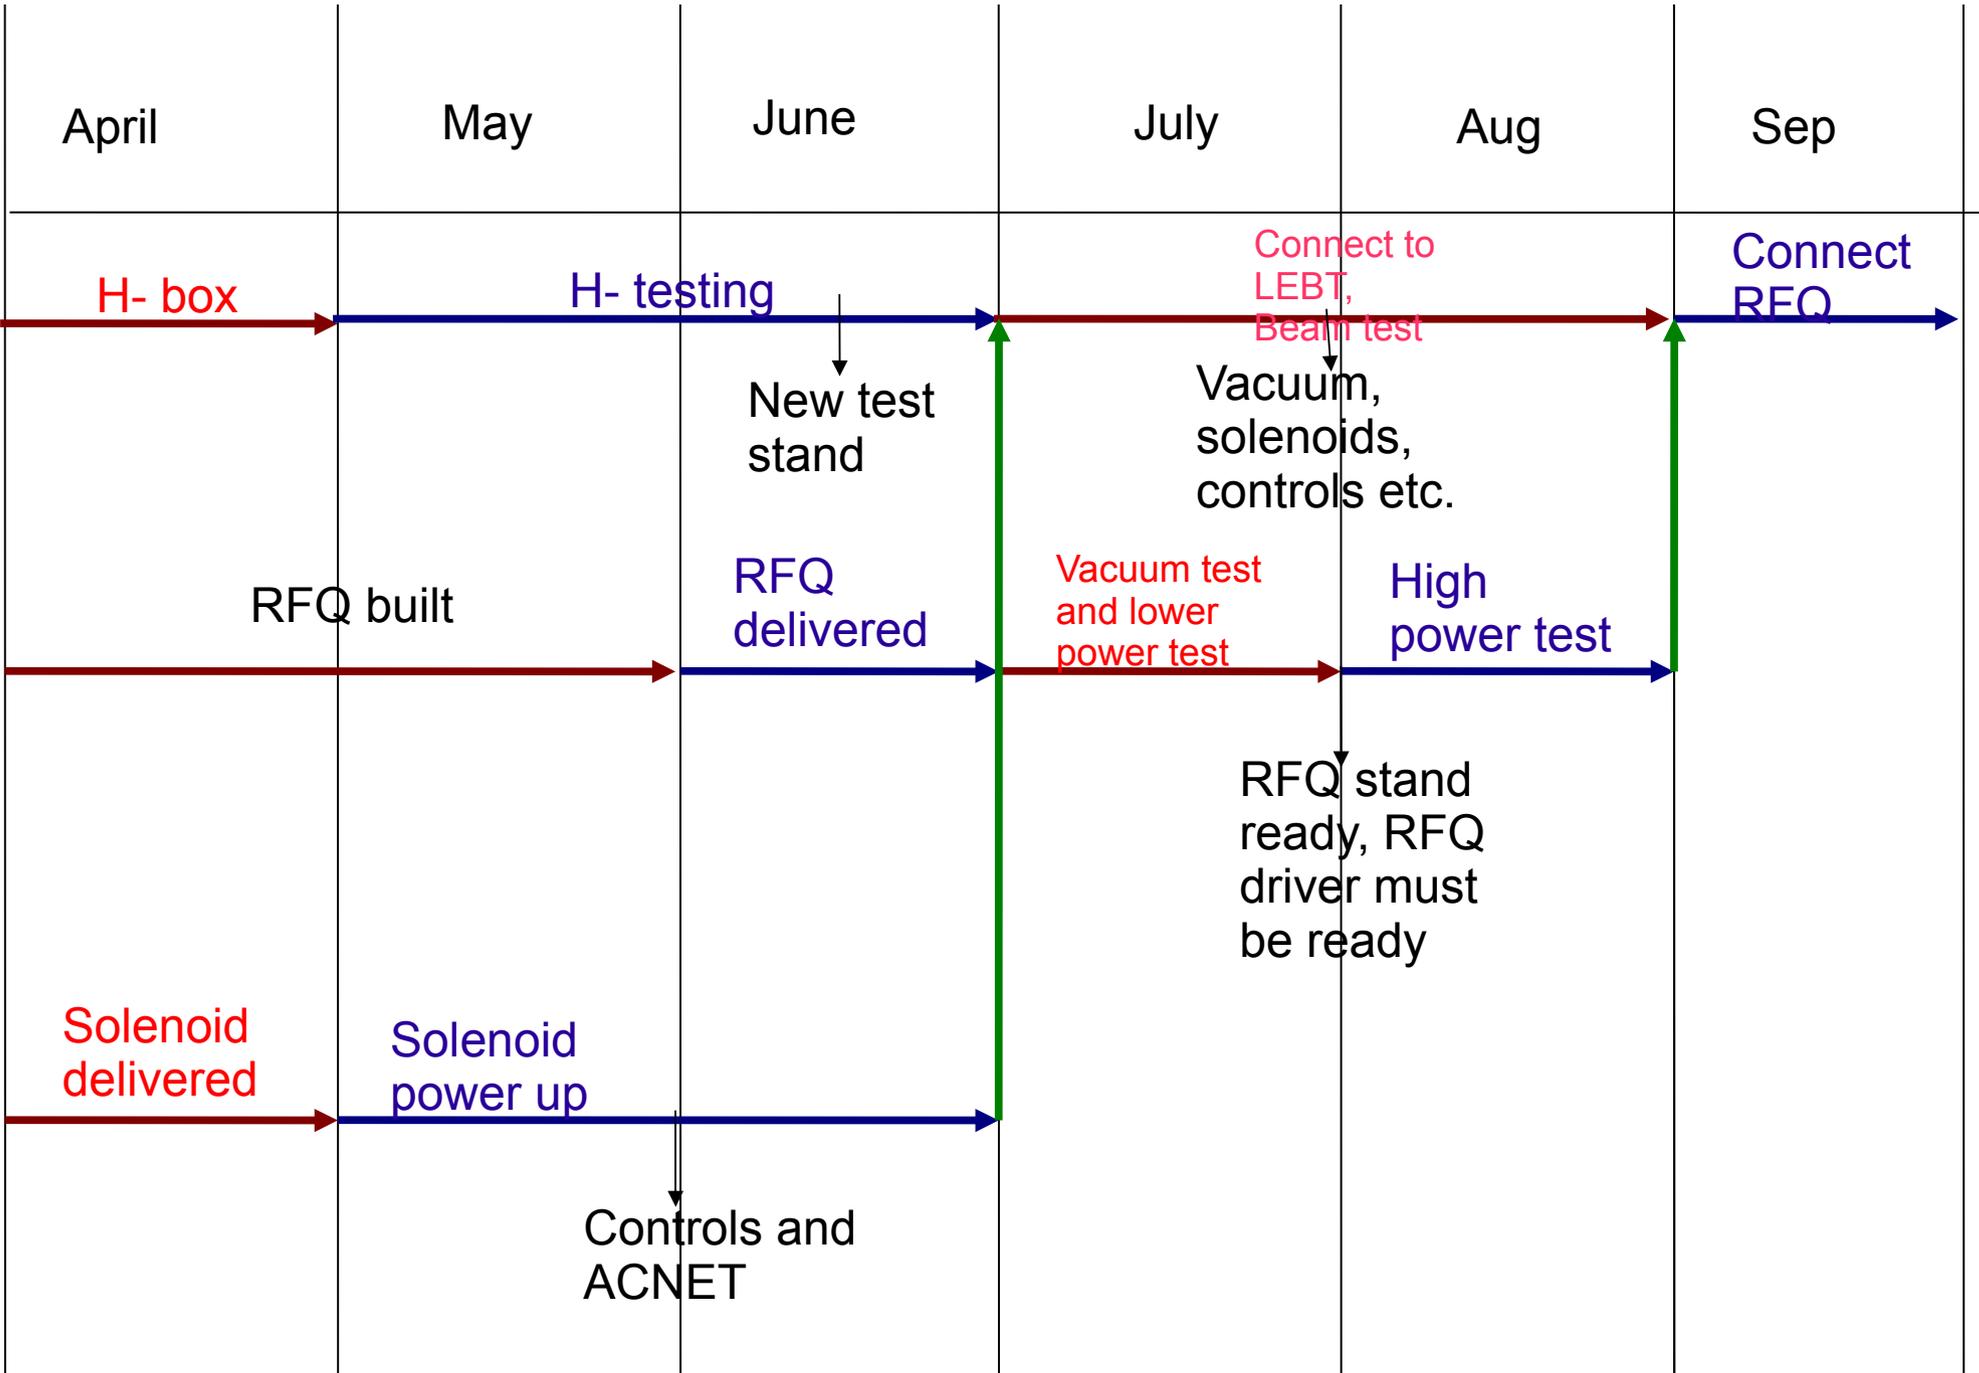

# Expected Timeline

- H- source testing
  - completed in old test stand May/June.
  - Completed in new test stand June/July
- Solenoid testing done in June.
- LEBT must be ready by July.
  - PS, controls, vacuum, instrumentation.
- Receive RFQ May/June.
  - Low power testing.
  - High power testing complete in July.
- Requires driver to be ready June/July.
  - Controls, vacuum.

# Time line continued.

- LEBT test with beam
  - Solenoid scans (No correctors) July.
  - Einzel lens test Aug.
  - Corrector scans Aug.
- Beam thru RFQ Sept.
  - Instrumentation.
  - 1<sup>st</sup> Quads should be here in Sept./Oct
